


Network Progress Report Inception to Year-to-Date

	July-Sept '10 Y1Q1	Oct-Dec '10 Y1Q2	Jan-March '11 Y1Q3	April-June '11 Y1Q4	July-Sept '11 Y2Q1
--	-----------------------	---------------------	-----------------------	------------------------	-----------------------

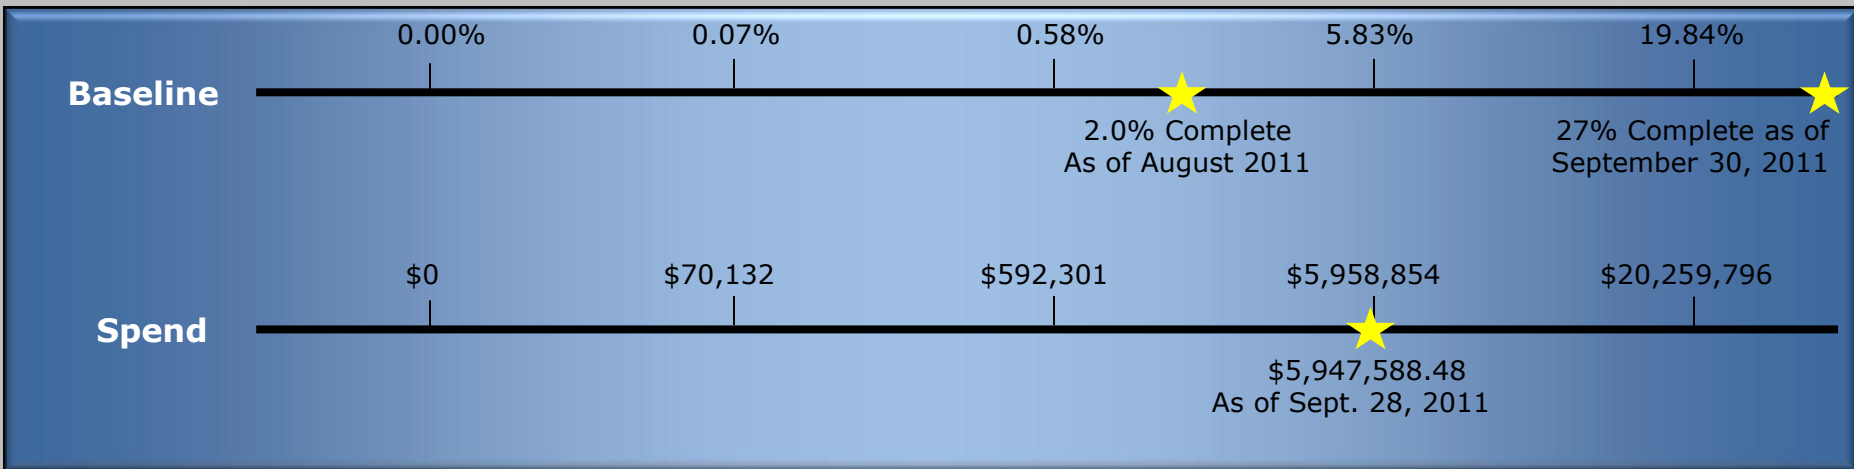


Milestones	July-Sept '10 Y1Q1	Oct-Dec '10 Y1Q2	Jan-March '11 Y1Q3	April-June '11 Y1Q4	July-Sept '11 Y2Q1
	<ul style="list-style-type: none"> Grant Award 	<ul style="list-style-type: none"> Staffing Website 	<ul style="list-style-type: none"> Staffing Database Development BTOP Partner Retreat Developed Deployment Strategy 	<ul style="list-style-type: none"> FPO Site Visit Network Design EA & FONSI CAI Site Contacts Redesign Telehealth Facilities to AREON 	<ul style="list-style-type: none"> MOAs Signed (51 of 99) 8 RFPs Posted 3 RFPs Awarded Public PCs New Identity - Arkansas e-Link AREON Management

Outreach Activity	July-Sept '10 Y1Q1	Oct-Dec '10 Y1Q2	Jan-March '11 Y1Q3	April-June '11 Y1Q4	July-Sept '11 Y2Q1
	<ul style="list-style-type: none"> Media Blitz 	<ul style="list-style-type: none"> 1 public presentation 	<ul style="list-style-type: none"> 2 public presentations 	<ul style="list-style-type: none"> 10 public presentations 	<ul style="list-style-type: none"> 3 public presentations CAI Packets CAI Site Visits

Network Progress Report Y2Q2 to Completion Projections

Oct-Dec Y2Q2	Jan-March Y2Q3	April-June Y2Q4	July-Sept Y3Q1	Oct-Dec Y3Q2	Jan-March Y3Q3	April-June Y3Q4	July-Sept Y4Q1
--------------	----------------	-----------------	----------------	--------------	----------------	-----------------	----------------

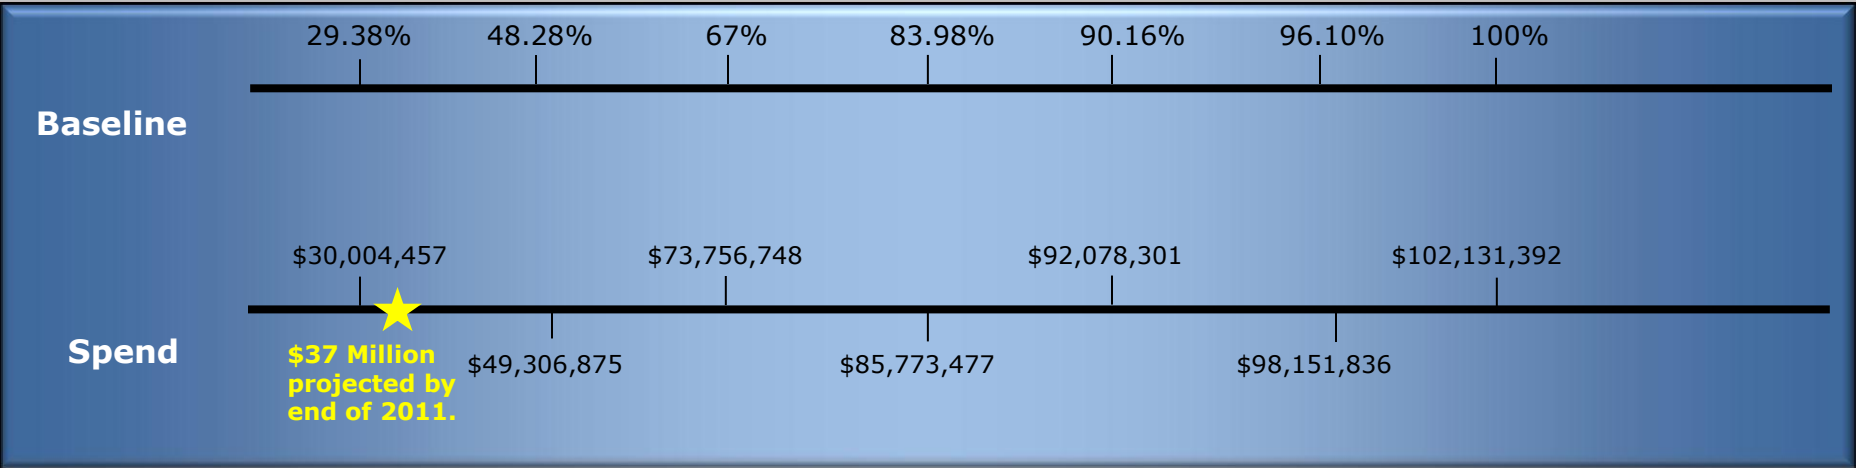

Milestones

- Equipment Delivery & Installation (Phase I) Oct-Dec 2011
- Equipment Delivery & Installation (Phase II) Jan-Dec 2012
- Broadband Installation and Broadband Upgrade (All Phases) Jan-Dec 2012
- Complete Construction Permits & Other Approvals
- Complete All RFPs/Contracts by January 2012
- Complete Network Build
- Sustainability Efforts

Outreach Activity

- SCTRC Site Visits for Training
- Project Managers Conduct 2 More Site Visits
